



MUHSEN

HAJJ OPERATIONAL PLAN

2027M / 1448H

SECTION 01 · INTRODUCTION

Muhsen Company Identity

The Objective

To provide real data to government related to Hajj and all the departments inside Holiday Inn to ensure seamless, efficient, and accessible services for pilgrims performing Hajj, ensuring their spiritual journey is safe, organized, and fulfilling through innovative technological solutions and dedicated support.

We strive to achieve the highest level of customer satisfaction through our dedication to noble Islamic values, and by serving pilgrims with sincerity, integrity, and excellence, drawing on our deep-rooted experience in the Hajj sector.


The Vision

To be pioneers in delivering a spiritual and comfortable Hajj experience that meets the highest standards of quality, with the ambition of ranking among the top five Hajj service providers in the Kingdom by the year 2030.

The Mission


To deliver high-quality services to pilgrims with continuous improvement based on international standards.

The Values

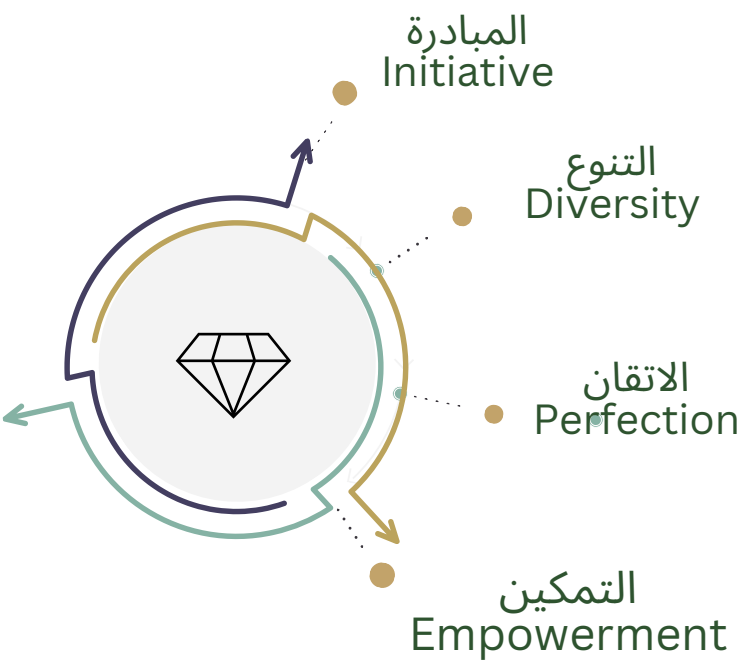

SECTION 02 · ORGANIZATIONAL CHART

Muhsen Organizational Chart

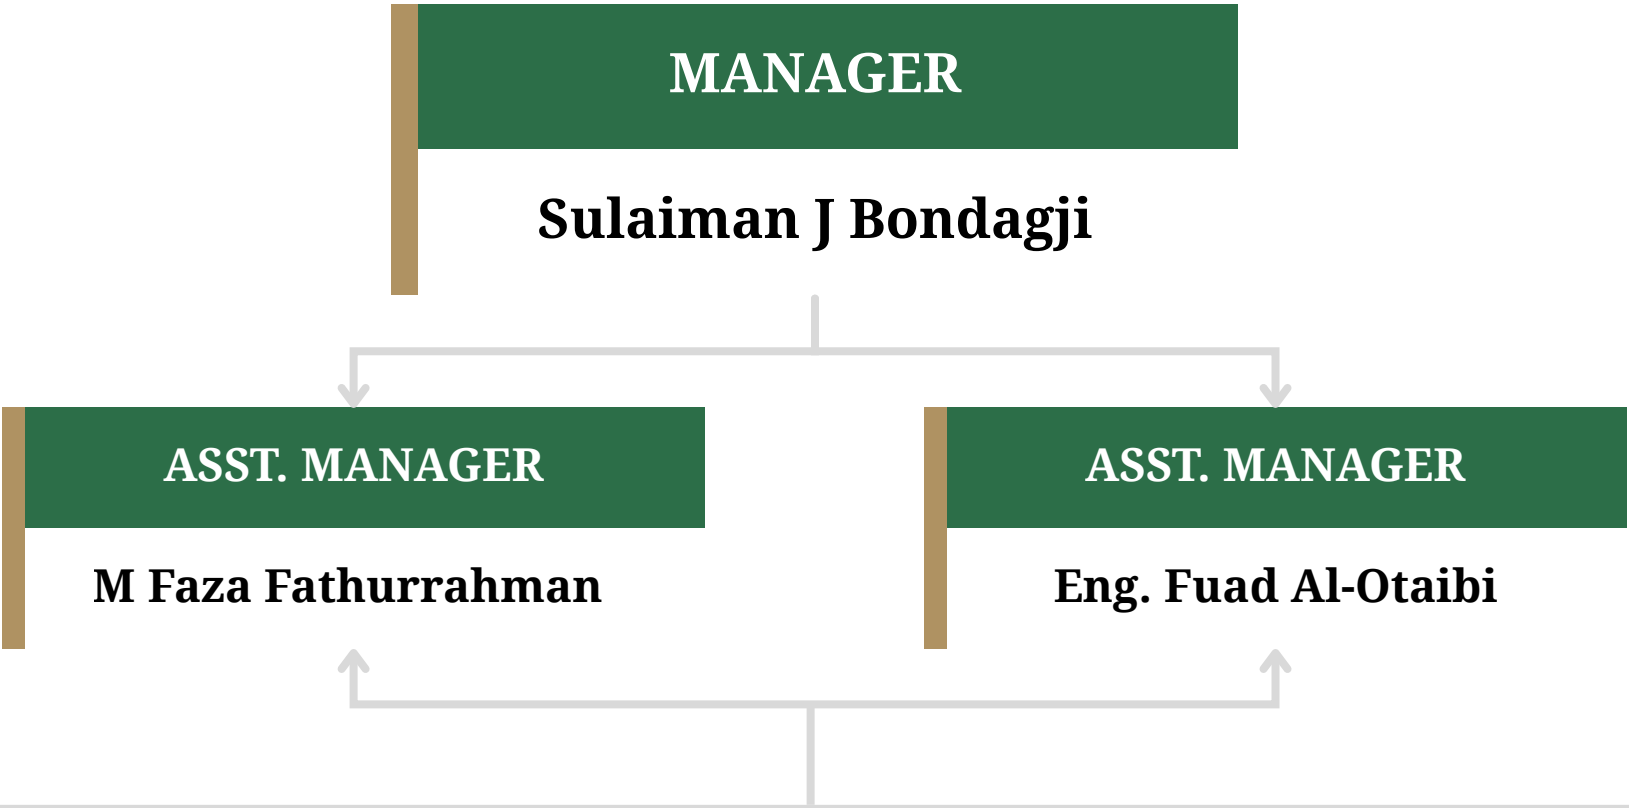

SECTION 03 · OPERATIONAL CALENDAR

Hajj Operational Timeline

28 Rabiul Tsani 09 October - Malaysia Hajj Carnival 20 Jumadil Awal 31 October - Hajj Conference and Exhibition	01 Rajab 10 December Ajeer & Muqeeem Regisration	15 Shaban 23 January - End Comprehensive Package contracting 20 Shaban 28 January - Start Visa Issuance	25 Ramadhan 04 March Start Nusuk Card Printing	01 Shawwal 09 March - End of Visa Issuance 15 Shawwal 24 March - End of Ajeer submission - Start workers registration	01 Dzul Qo'dah 07 April - First Arrival Pilgrims - Mina Readiness 15 Dzul Qo'dah 21 April - Arafah Readiness 29 Dzul Qo'dah 06 May - Last Camp Inspection Visits	06 Dzul Hijjah 12 May - Last Pilgrims Arrival 07 Dzul Qo'dah 13 May - First Movement to Mashaer	01 Muharam 06 June - Handover Completion Certificate 15 Muharam 20 June - Last Pilgrims Departure
Jumadil Awal	Rajab	Sha'ban	Ramadhan	Shawwal	Dz Qo'dah	Dz Hijjah	Muharram
20 Jumadil Awal 31 October - Start of Pacakge Submission - Package Details - Total Pilgrims - Hotel Makkah - Hotel Madinah - Transportation - Catering - Mashaer Camp - Mashaer Package	01 Rajab 10 December - Mandub Registration - Mandub Details - Name - Iqamah - Passport - Self Portrait - DOB - Gender	10 Shaban 18 January - End of Nozoly Masar submission - Start Pilgrims Grouping	10 Ramadhan 17 February - End Pilgrims Grouping - Starts of Itineray Submission - Flight info - Pilgrims Manifest - Flight - Bus - Activities - Umrah - City Tour - Raudhah	05 Shawwal 14 March - Start of Nusuk Delivery 10 Shawwal 19 March - End of Mandub registration 25 Shawwal 29 March - End of Delivering Nusuk to Pilgrims' countries	01 Dzul Qo'dah 07 April - Start Mashaer add-on services request 25 Dzul Qo'dah 02 May - End of Mashaer add-on services request - Start of Mashaer Itinerary Submission - Mashaer Movement - Tarwiyah - Mabit / Murur - Jamarat - Ifadhah - Wada' - Mashaer Catering - BLD - Special Request	02 Dzul Hijjah 08 May - Camp Handover to Hajj Mission, PJH, PIHK 03 Dzul Hijjah 09 May - End of Mashaer Itinerary Submission - Final Mashaer Movement - Final Mashaer Catering - Early Departure Information 06 Dzul Hijjah 12 May - First workers movement to Mashaer	20 Muharam 25 June End of Evaluation

Hajj Operational Timeline

From package readiness to camp handover • October 2026 – May 2027

[illegible]

SECTION 03 · OPERATIONAL CALENDAR

Hajj Operational Timeline

PHASE 1

Packaging & Registration

31 OCT - 19 MAR

Package Submission

GREGORIAN
18 Oct → 18 Jan

HIJRI
20 Jumadil Awal → 10 Sha’ban

Window ≈ 80 days

Mandub Registration

GREGORIAN
10Dec → 19 Mar

HIJRI
01 Rajab → 10 Shawwal

Window ≈ 100 days

PHASE 2

Grouping & Itinerary

18 JAN — 29 MAR

Pilgrims Grouping

GREGORIAN
18 Jan → 17 Feb

HIJRI
10 Sha’ban → 10 Ramadhan

Window ≈ 31 days

Itinerary Submission

GREGORIAN
17 Feb → 29 Mar

HIJRI
10 Ramadhan → 25 Shawwal

Window ≈ 41 days

PHASE 3

Add-On and Permits

18 JAN — 29 MAR

Additional Services Request

GREGORIAN
07 Apr → 02 May

HIJRI
01 → 25 Dzul Qa’dah

Window ≈ 25 days

Vehicle Permit Request

GREGORIAN
07 Apr → 02 May

HIJRI
01 → 25 Dzul Qa’dah

Window ≈ 25 days

PHASE 4

Mashaer & Handover

02 MAY — 12 MAY

Mashaer Itinerary Submission

GREGORIAN
02 May → 08 May

HIJRI
25 Dzul Qa’dah → 02 Dzul Hijjah

Window ≈ 6 days


Camp Handover

GREGORIAN
08 May → 12 May

HIJRI
02 → 06 Dzul Hijjah

Window ≈ 5 days

SECTION 03 · CORE SYSTEM
Nozoly Core System Architecture

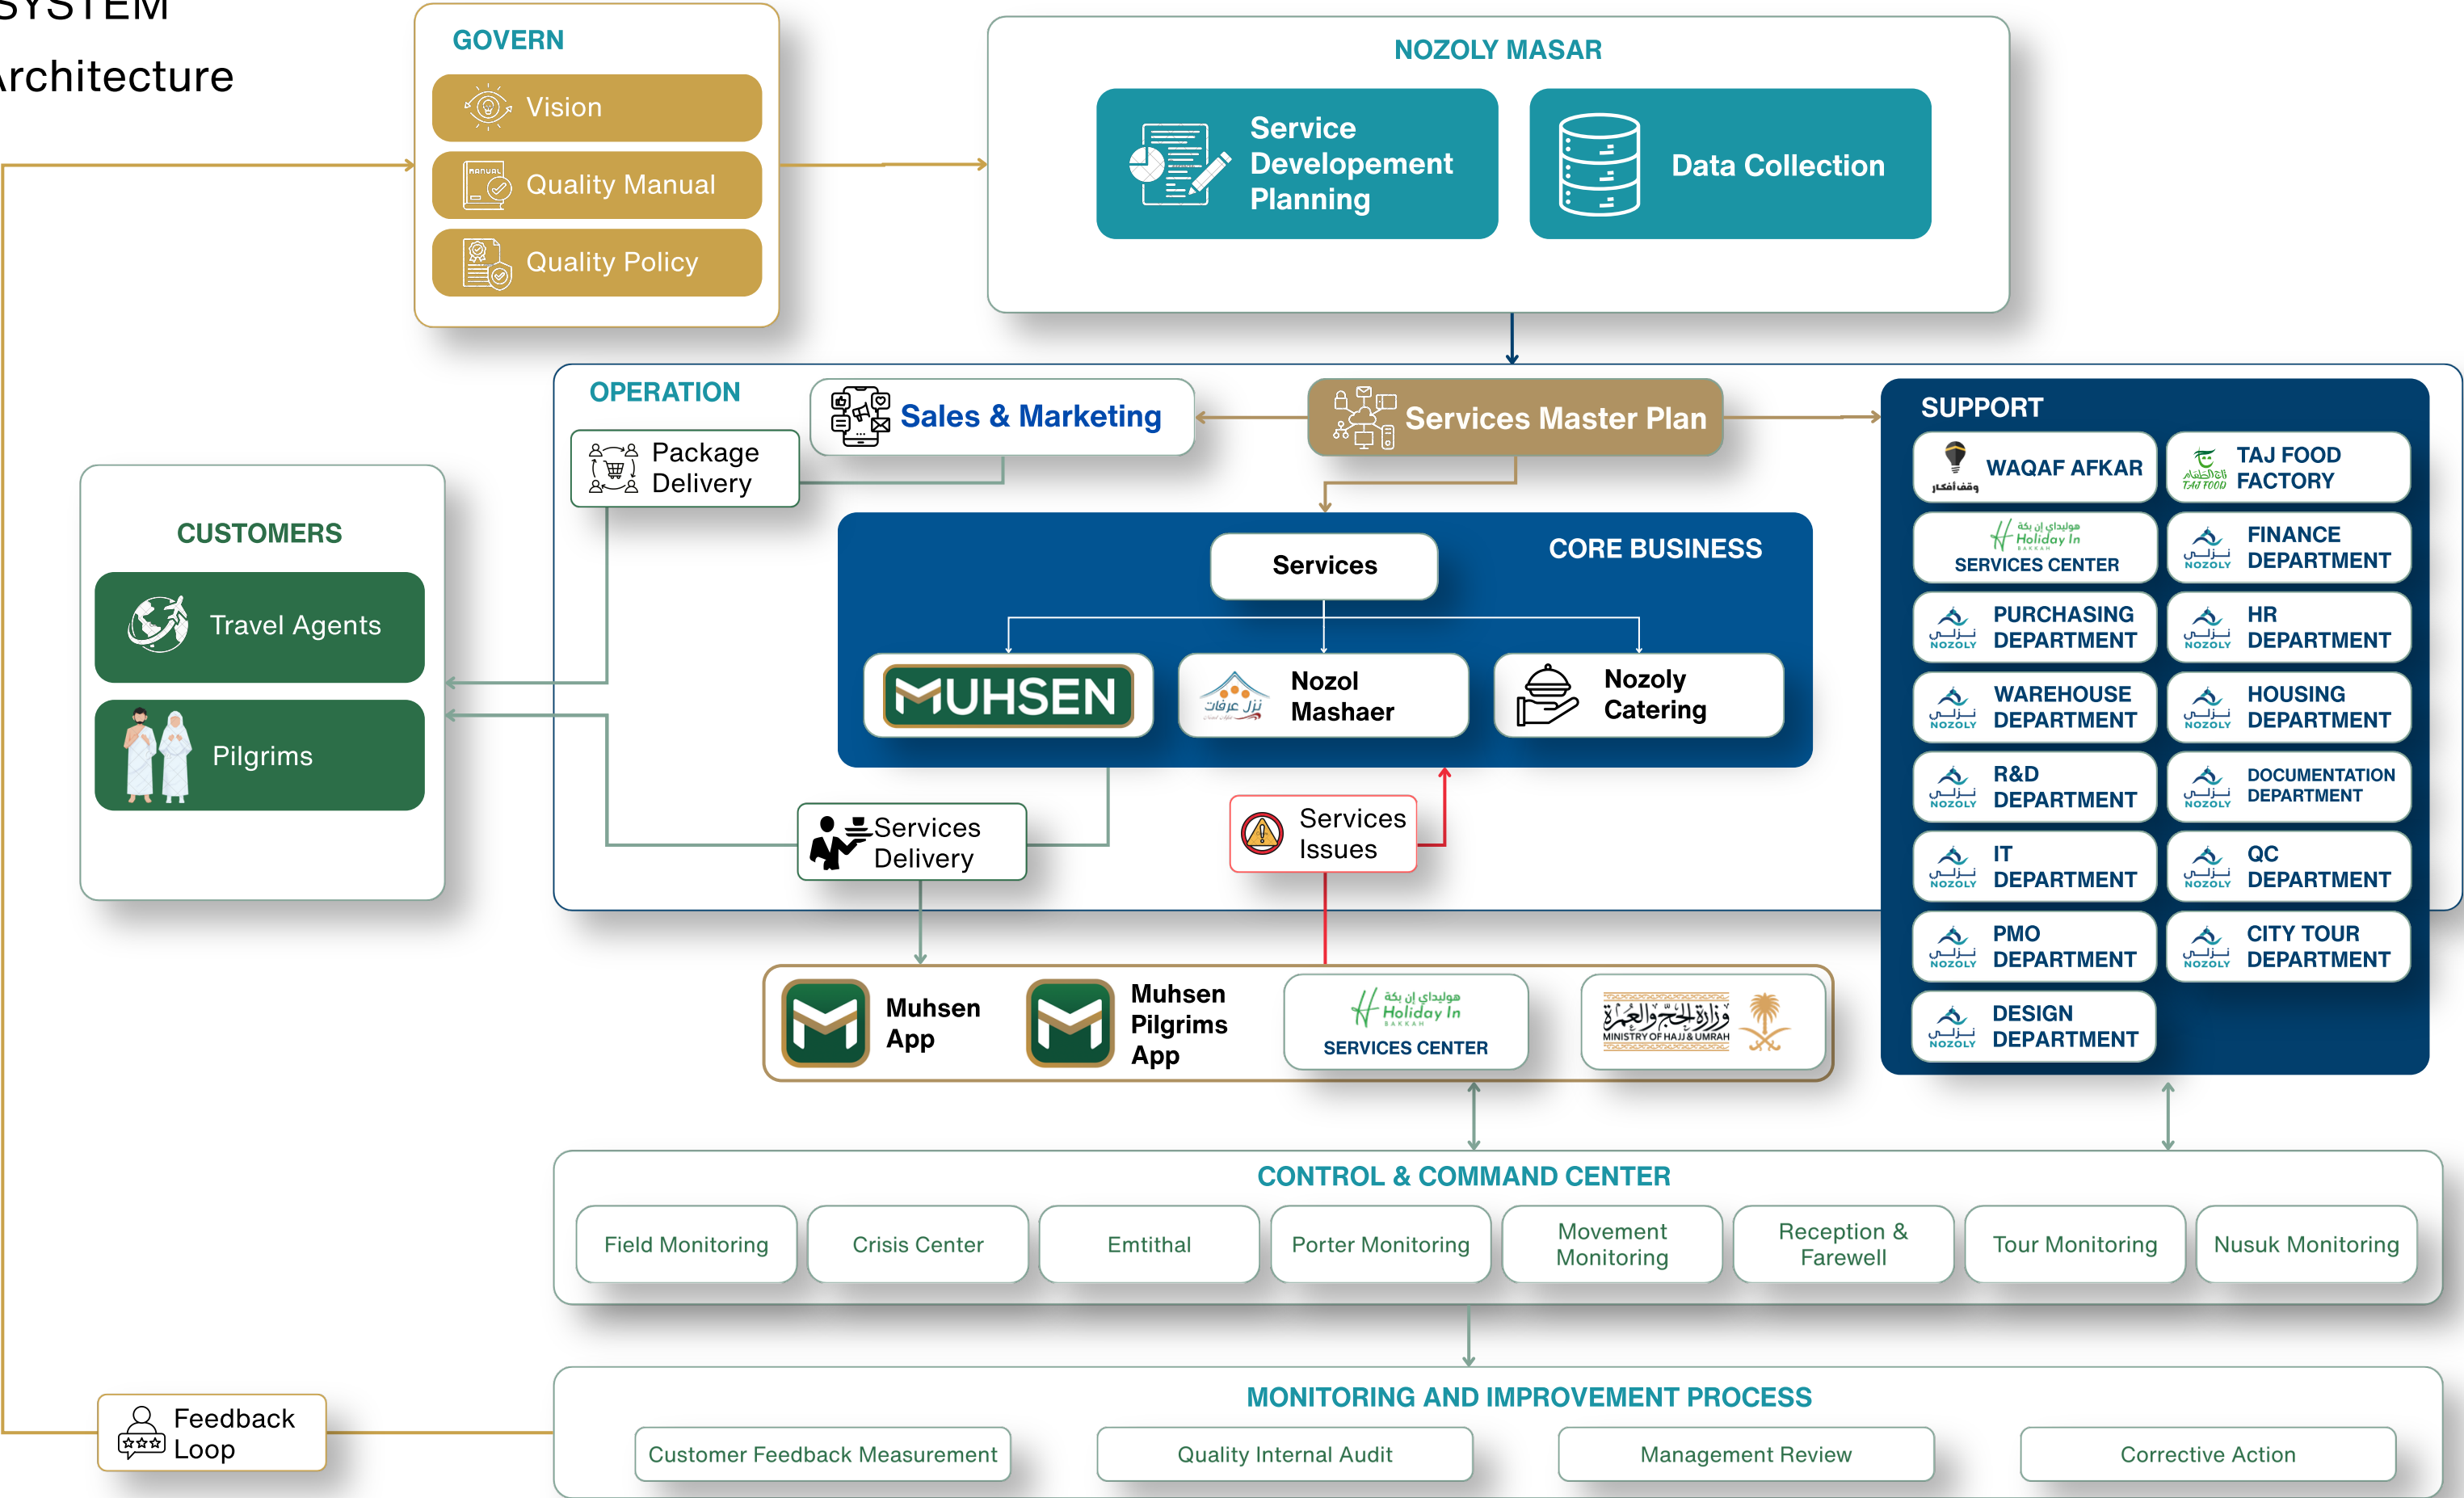

SECTION 04 · CONTENTS

Muhsen Operational Contents

Five Operational Workstreams working through One Integrated Delivery Model

01

International
Relation

02

Nozoly Masar

03

MUHSEN
Operation

04

Control &
Command
Center


05

Nusuk Card
Distribution


SECTION 04 - A · INTERNATIONAL RELATIONS

Assumed Clients and Total Pilgrims

Pilgrims by Countries

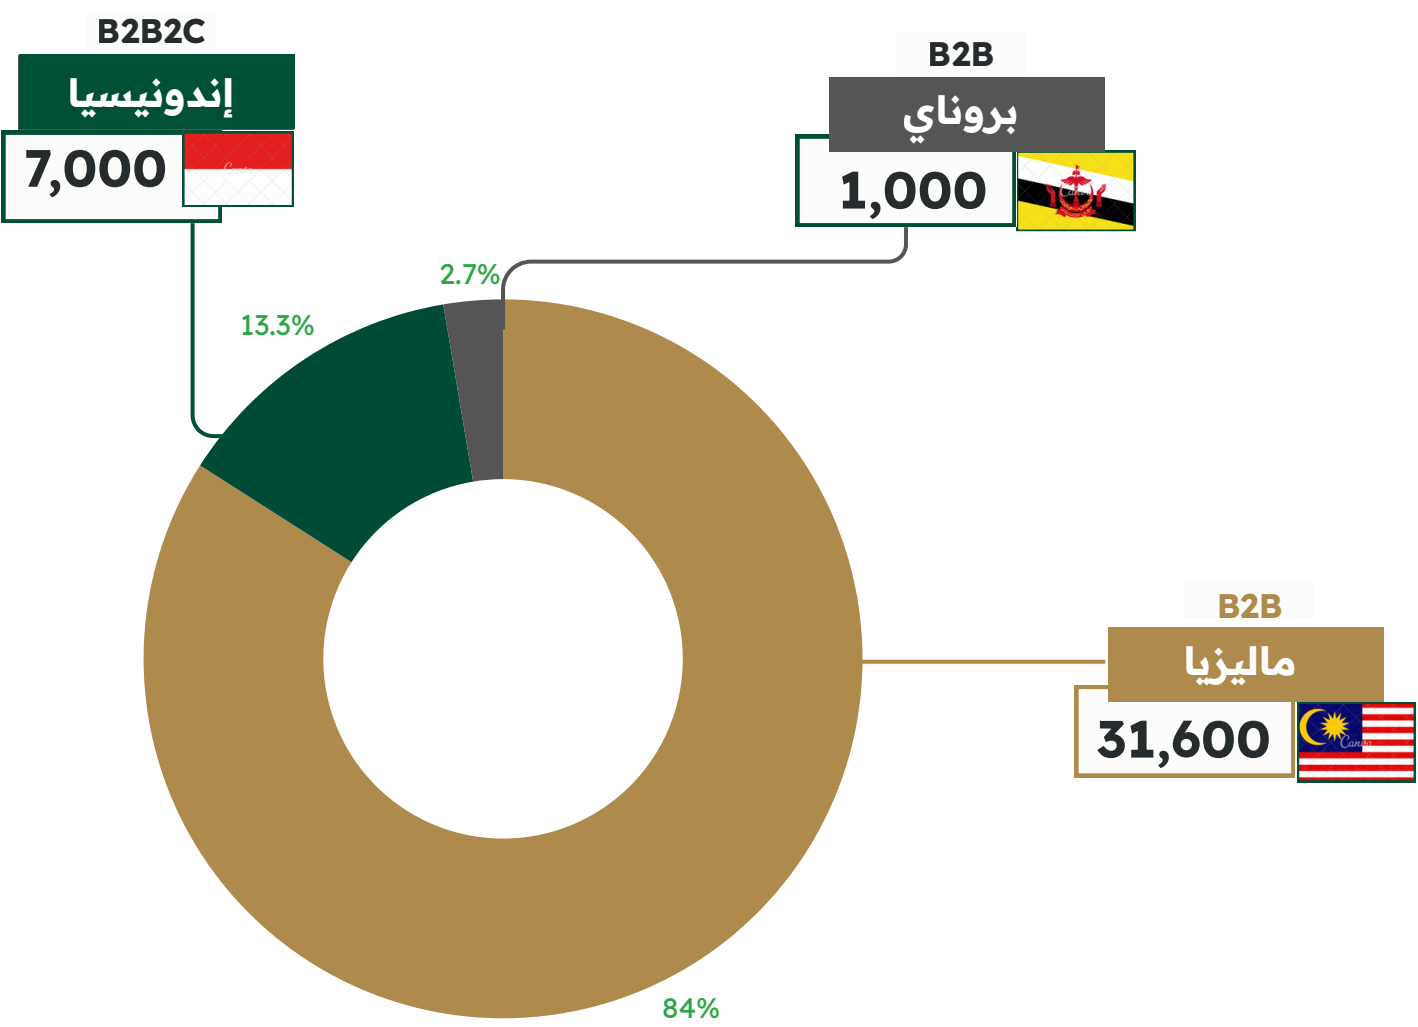





Companies by Countries

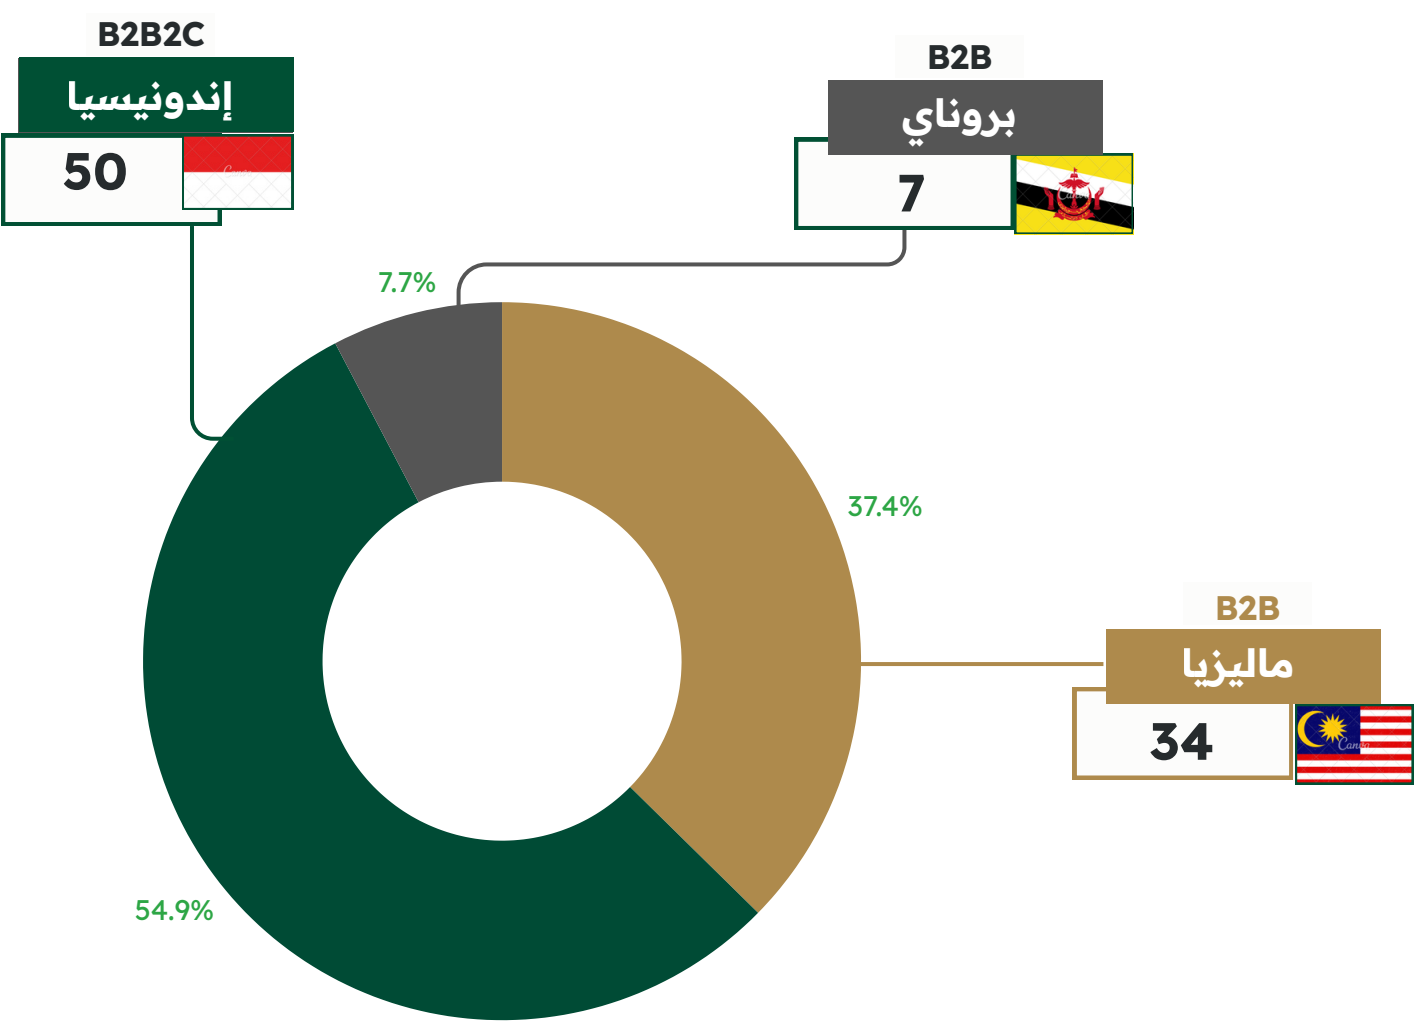


SECTION 04 - B.01 · NUSUK MASAR
One Stop Submission System

Nozoly Masar

Nozoly has developed a dedicated digital platform aligned with the structure and data requirements of Nusuk Masar. It collects, validates, and consolidates every submission before it moves forward.

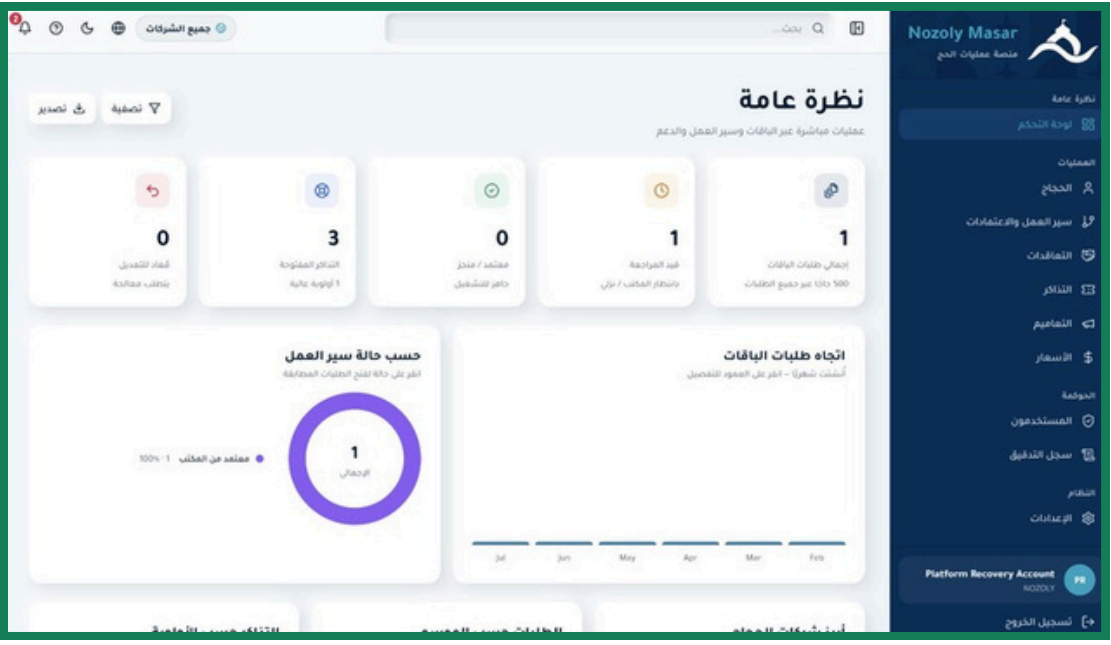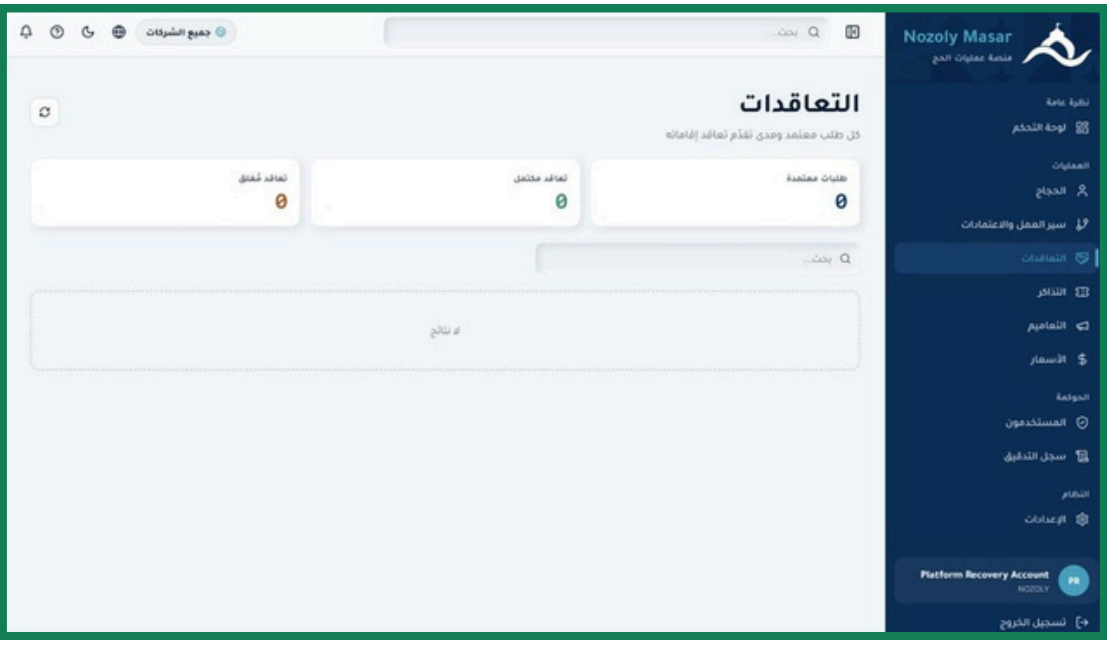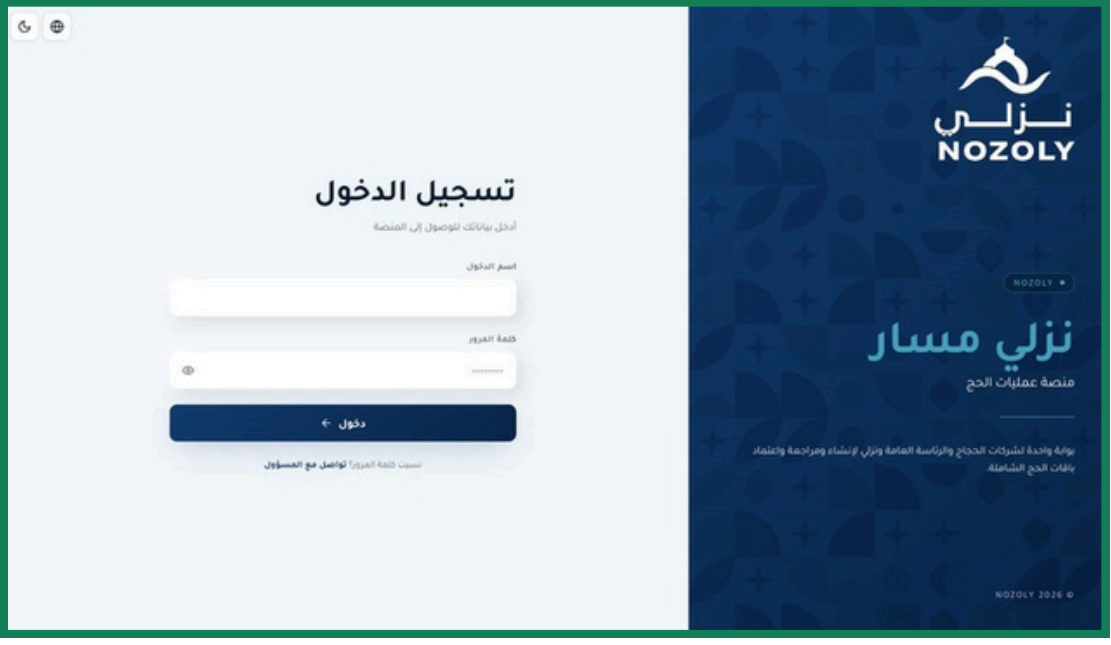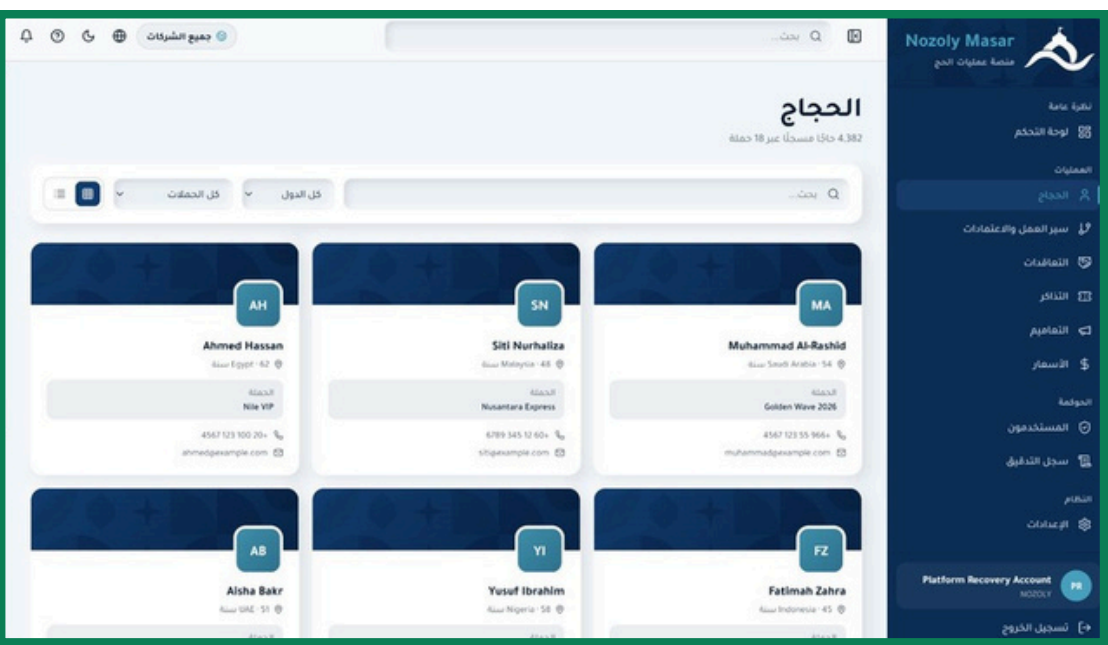

SECTION 04 - B.02 · NUSUK WORKFLOW
End-to-End Seamless Integration

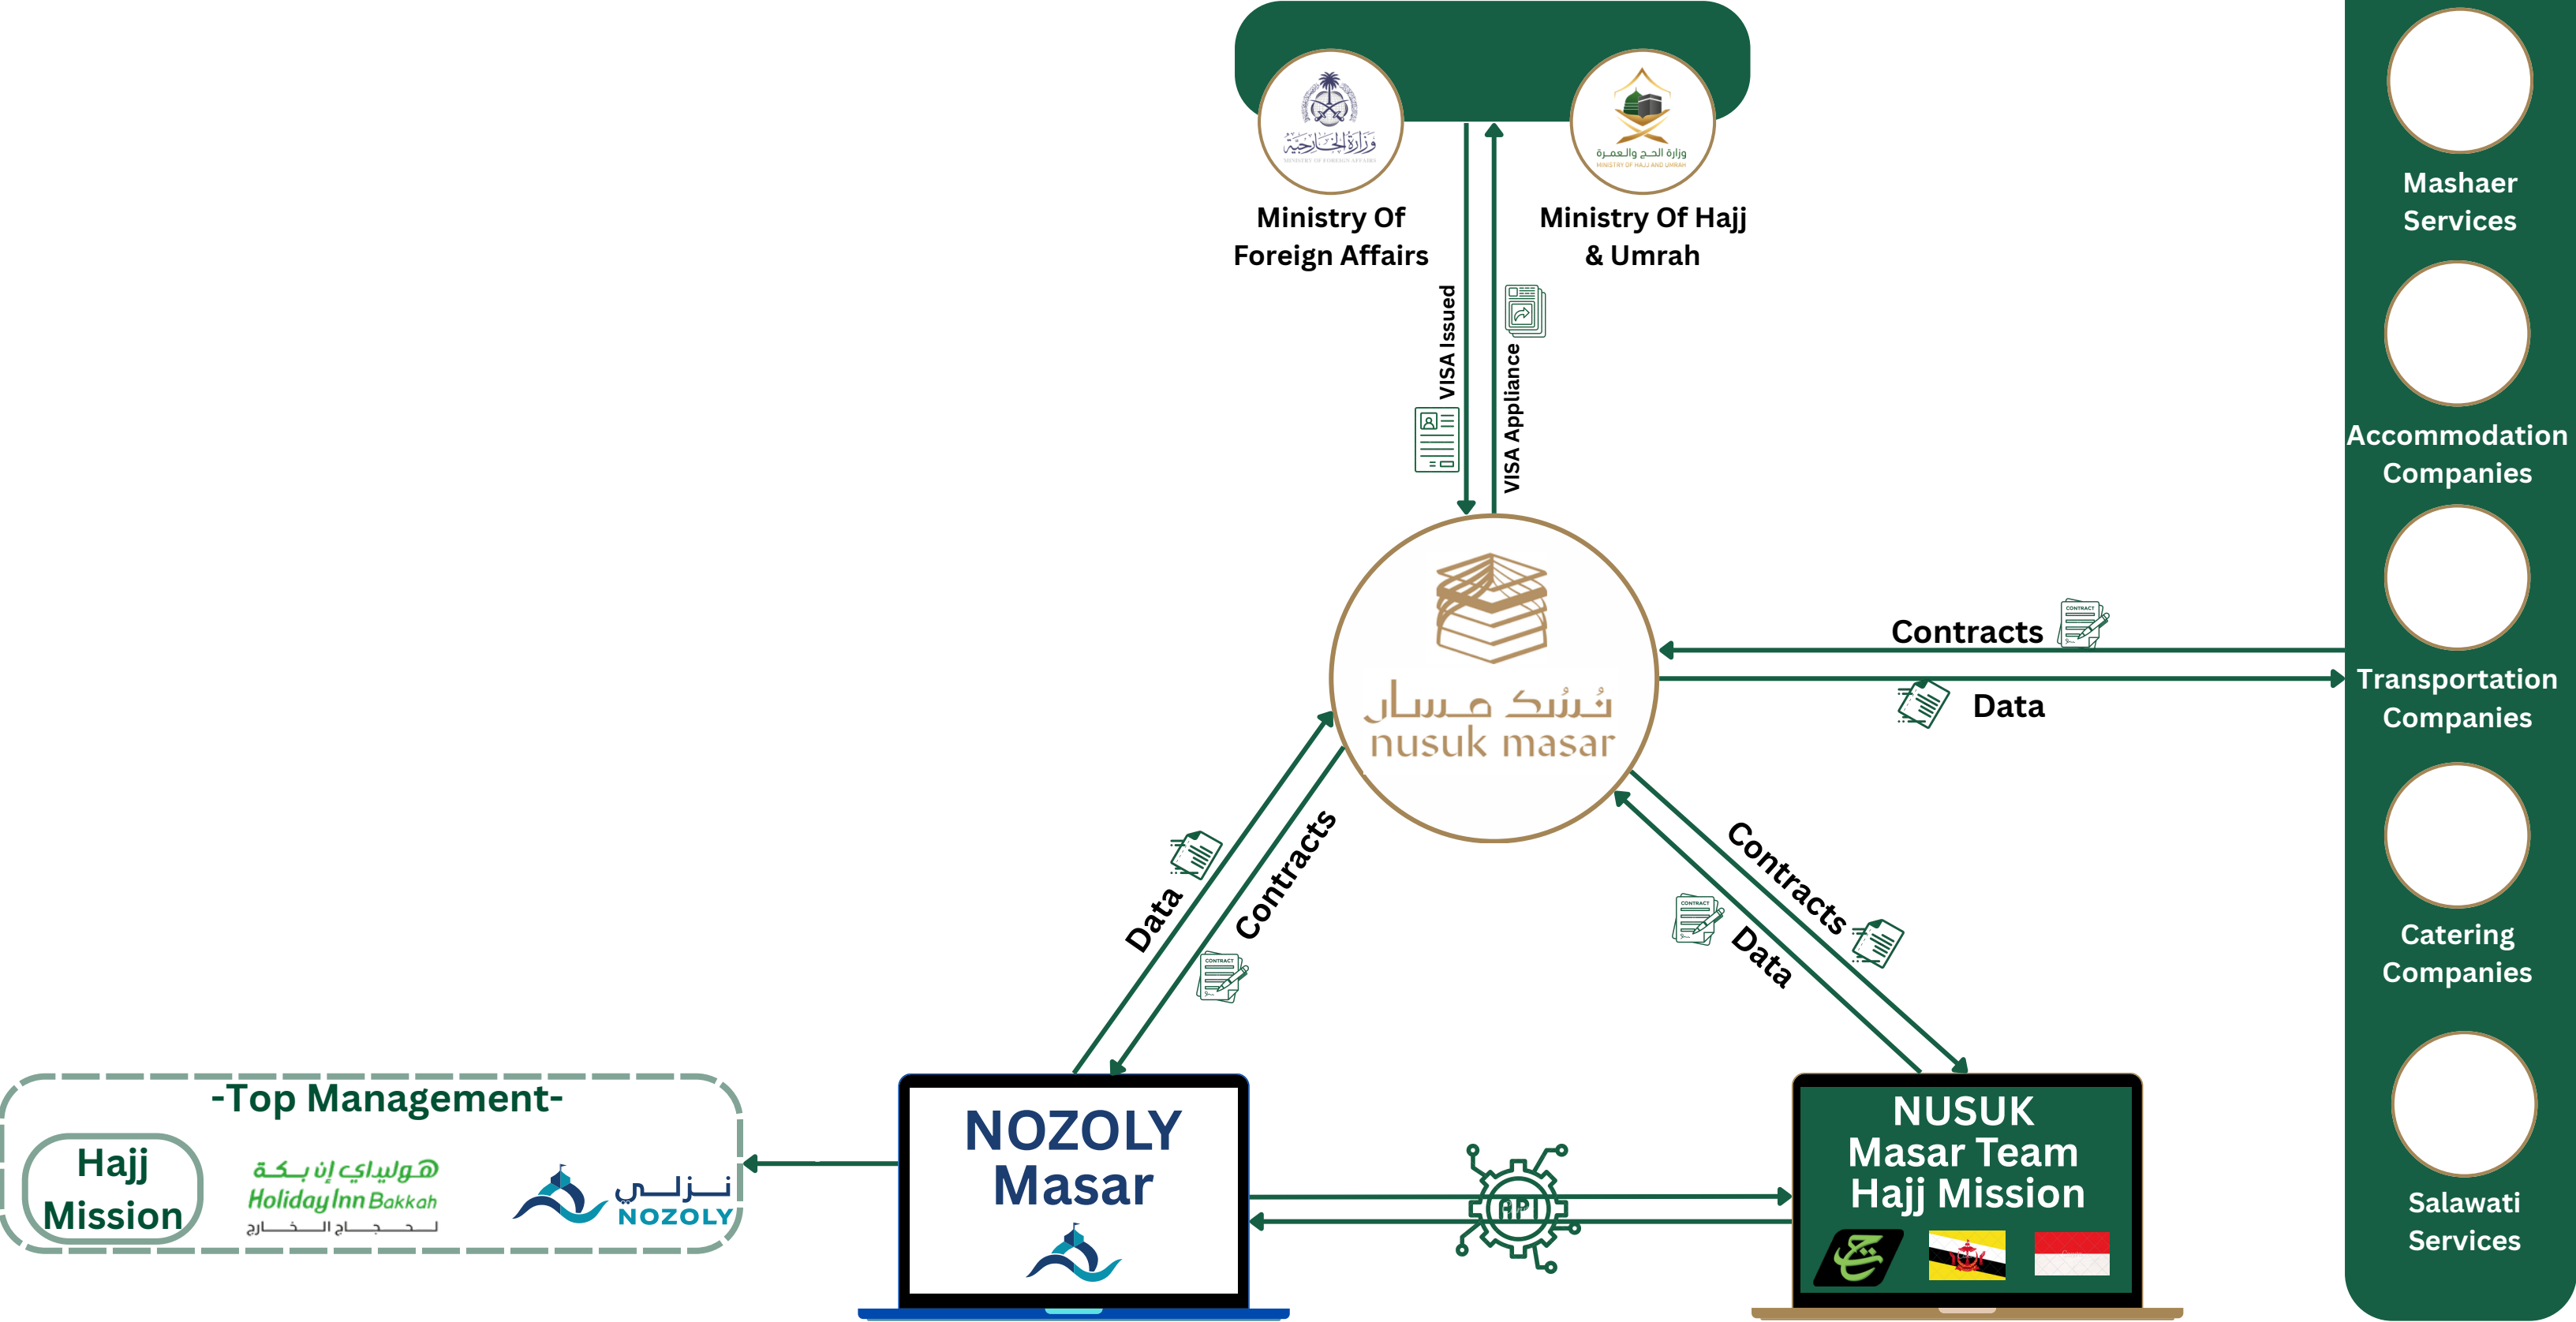

SECTION 04 - B.03 · DATA COLLECTION

Big Data System & Analytical

01

Pilgrims Informations

- Haji Name
- Gender
- Date of Birth
- Passport Number
- Visa Number
- Passport Issue & Expiry Dates
- Phone Number
- Email
- Address
- Health Status
- Pilgrim's Barcode
- Pilgrim's Photo
- Passport PDF
- MCU
- Insurance Number

Purpose

- To analyze the male/female ratio for MUHSEN staff allocation.
- To send awareness messages via SMS and email.
- To plan the executive health program.
- To simulate the pilgrim's ID card and integrate the barcode with the MUHSEN system.

02

Flight Informations

- KT Number
- Flight Number
- Departure Date/Time
- Arrival Date/Time

Purpose

- To support the operational planning of MUHSEN, Catering, Housing, and Transportation departments.
- To synchronize MUHSEN teams schedules.

03

Pilgrims Manifest

- Number of buses
- Flight Manifest
- Bus Manifest

Purpose

- To assign MUHSEN Leaders
- To Assign MUHSEN members

04

Housing Informations

- Hotel Name
- Hotel Location
- Check-in/Check-out Dates and Times
- Total Number Rooms
- Room Number per pilgrims

Purpose

- To prepare the housing plan.
- To determine the pilgrims' duration of stay in Madinah and Makkah.
- To plan MUHSEN staff accommodation and catering requirements.

05

Transportation Infomations

- Company Name
- Transportation Route
- Total Transportation
- Type of Transportation

Purpose

- To strategize the movement operation
- To evaluate the route information and processes

06

Mashaer Informations

- Movement Information
- Catering Information
- Camp Distribution

Purpose

- To plan the Transportation and Catering departments' operations.

07

City Tour Informations

- Tour destination points at Makkah, Madinah, Jeddah and Thaif
- Numbers of Pilgrims per tour

Purpose

- To design suitable city tour programs for Malaysian pilgrims.

08

Catering Information

- Catering Companies Details
- Contract Start - End date
- Price
- Service Location

Purpose

- To plan operations for the catering departments
- To strategize the distribution for the pilgrims

SECTION 04 - C.01 · MUHCEN OPERATION

Muhsen Field Teams



MUHCEN Management



M U H S E N
Per Bus



MUHCEN
Leader
Per KT




MUHCEN SPV
Per Hotel

SECTION 04 - C.02 · MUHSEN OPERATION

Muhsen Teams Distribution

Total Pilgrims	22,020
Total KT	76
Total MUHSEN	456

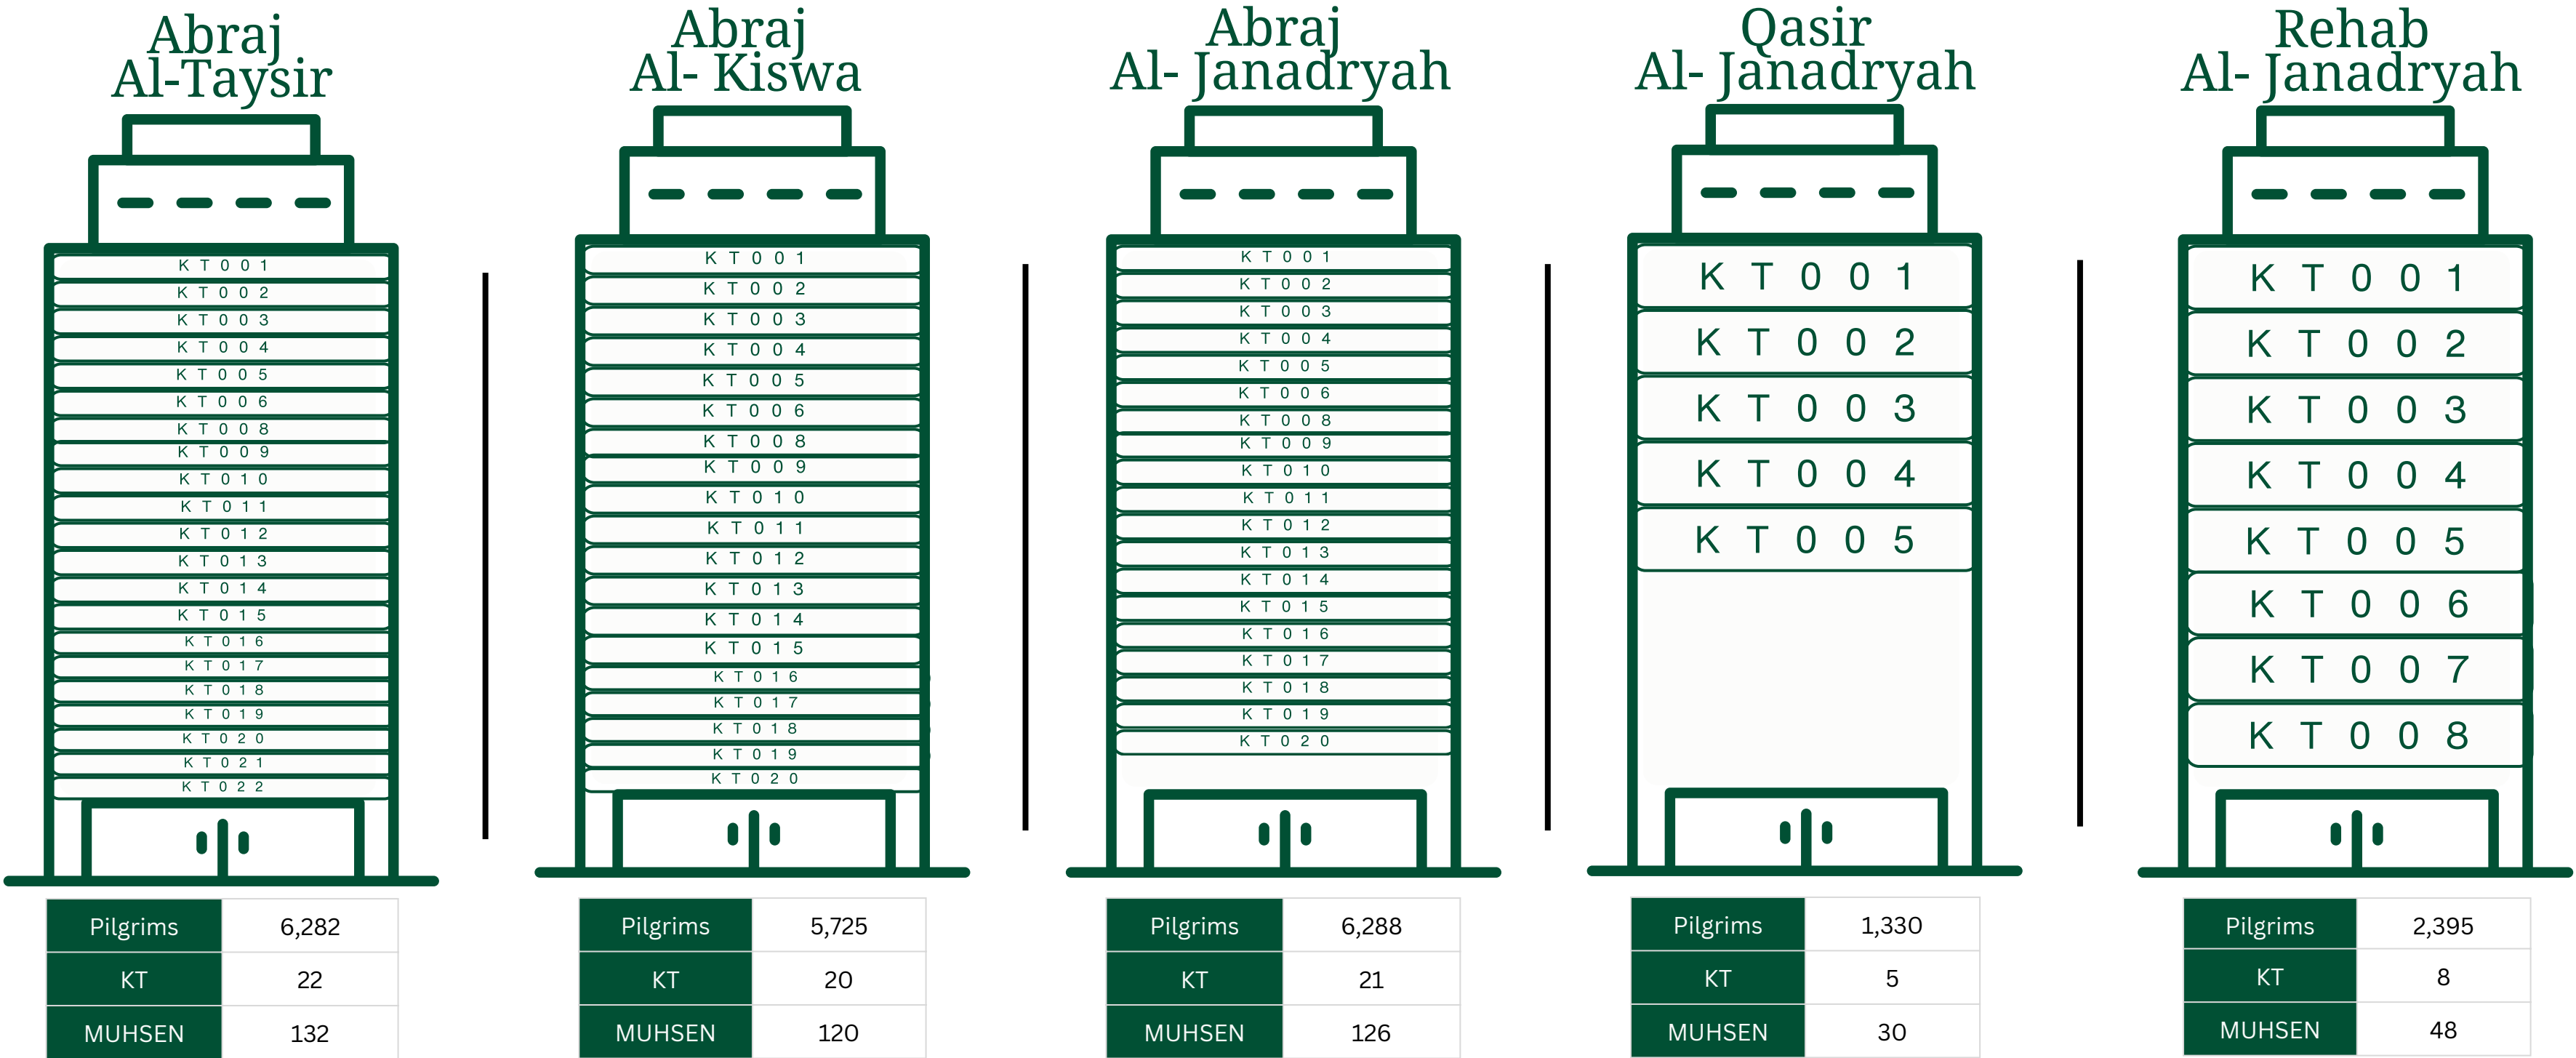


SECTION 04 - C.03 · MUHSEN OPERATION

Muhsen Standard Operation



MUHSEN
SPV

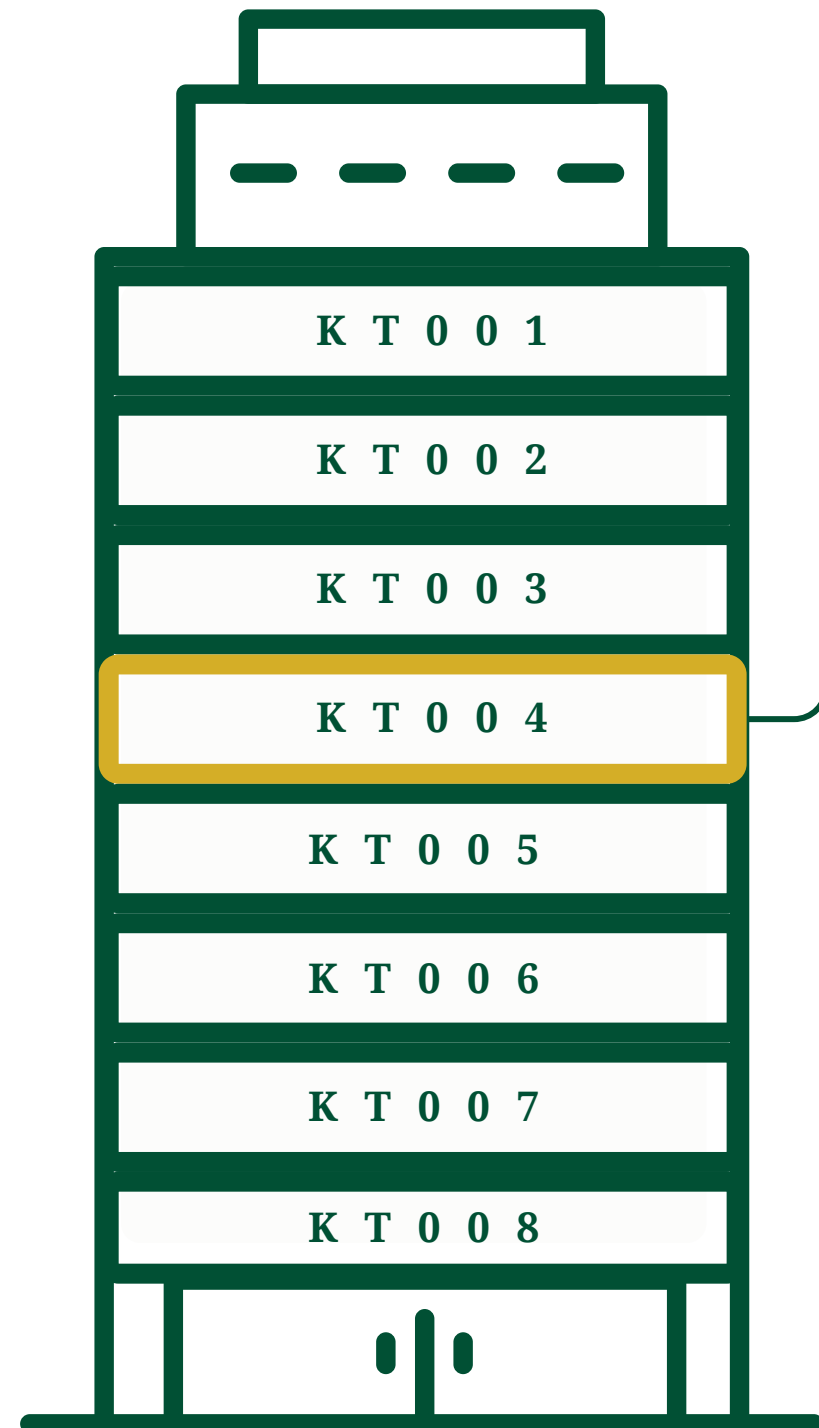

مهام مُحسن في مكة المكرمة:



- كشف الجاهزية
- إستلام الامتعة
- توزيع الوجبات
- الإستقبال
- عمرة القدوم
- المتابعة الميدانية اليومية
- تسليم الامتعة والوجبات (المغادرة)
- توديع الحجاج
- مرافقة الحجاج للمزارات
- ارشادات الطواف والسعي
- طواف الوداع

SECTION 04 - C.04 · MUHSEN OPERATION

Muhsen Standard Operation




MUHSEN
SPV

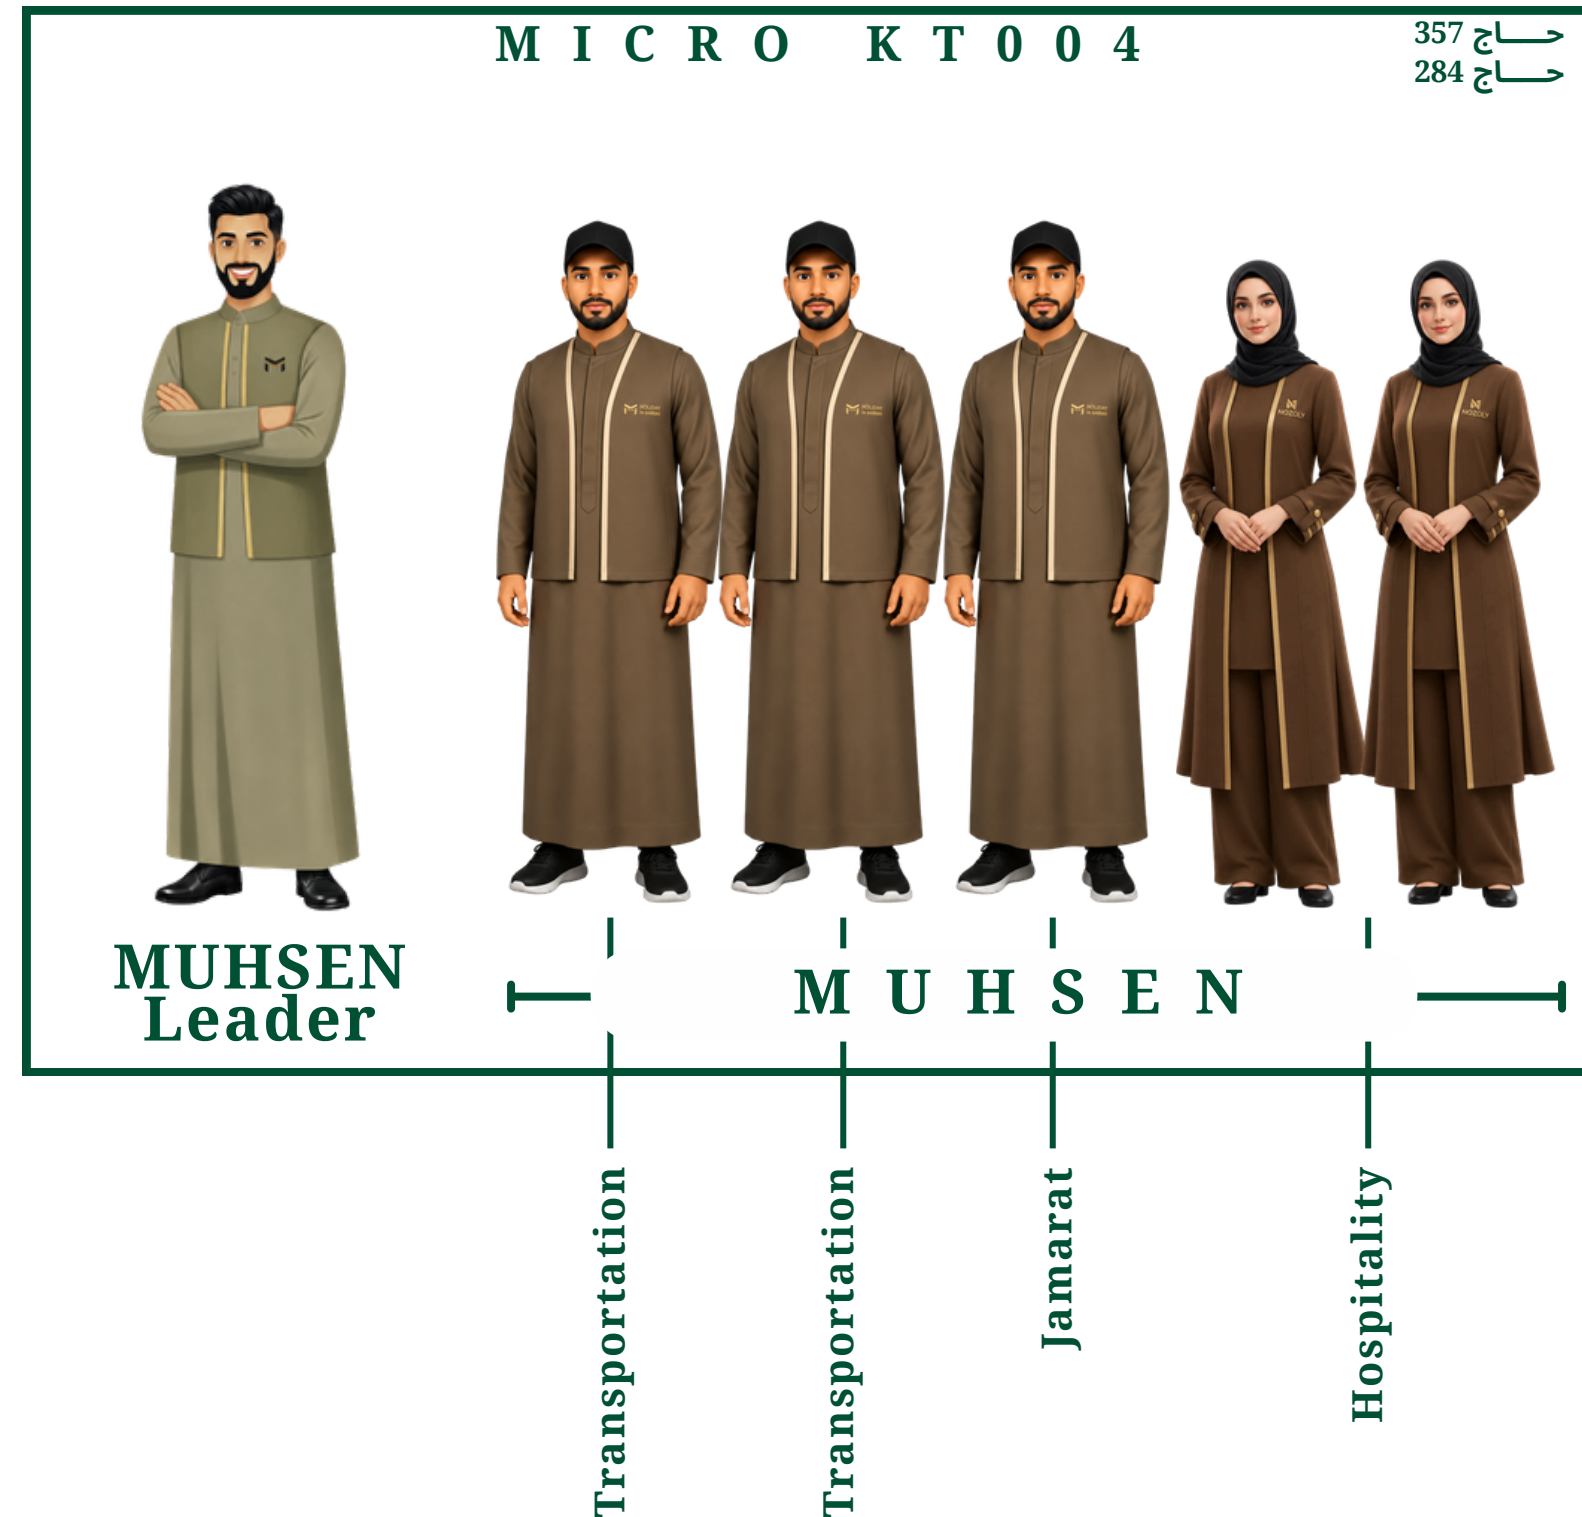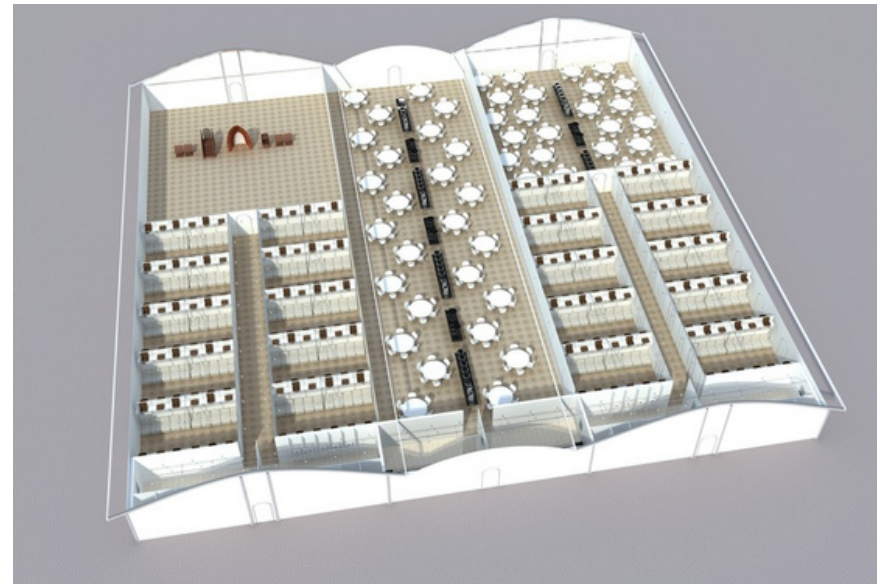

- مهام مُحسن في
المشاعر المقدسة:**
- تأكيد جاهزية
المشاعر (تعبئة
نماذج الوزارة)
 - استلام الباصات
 - نقل من الفندق الى
عرفة
 - ضيافة يوم 8
 - يوم عرفة
 - نقل من عرفة الى
مزدلفة او منى
 - ضيافة مزدلفة
 - نقل من مزدلفة الى
منى
 - ضيافة منى
 - جمرات
 - نقل من منى الى
مكة

SECTION 04 - C.04 · MUHSEN OPERATION

Muhsen Standard Operation

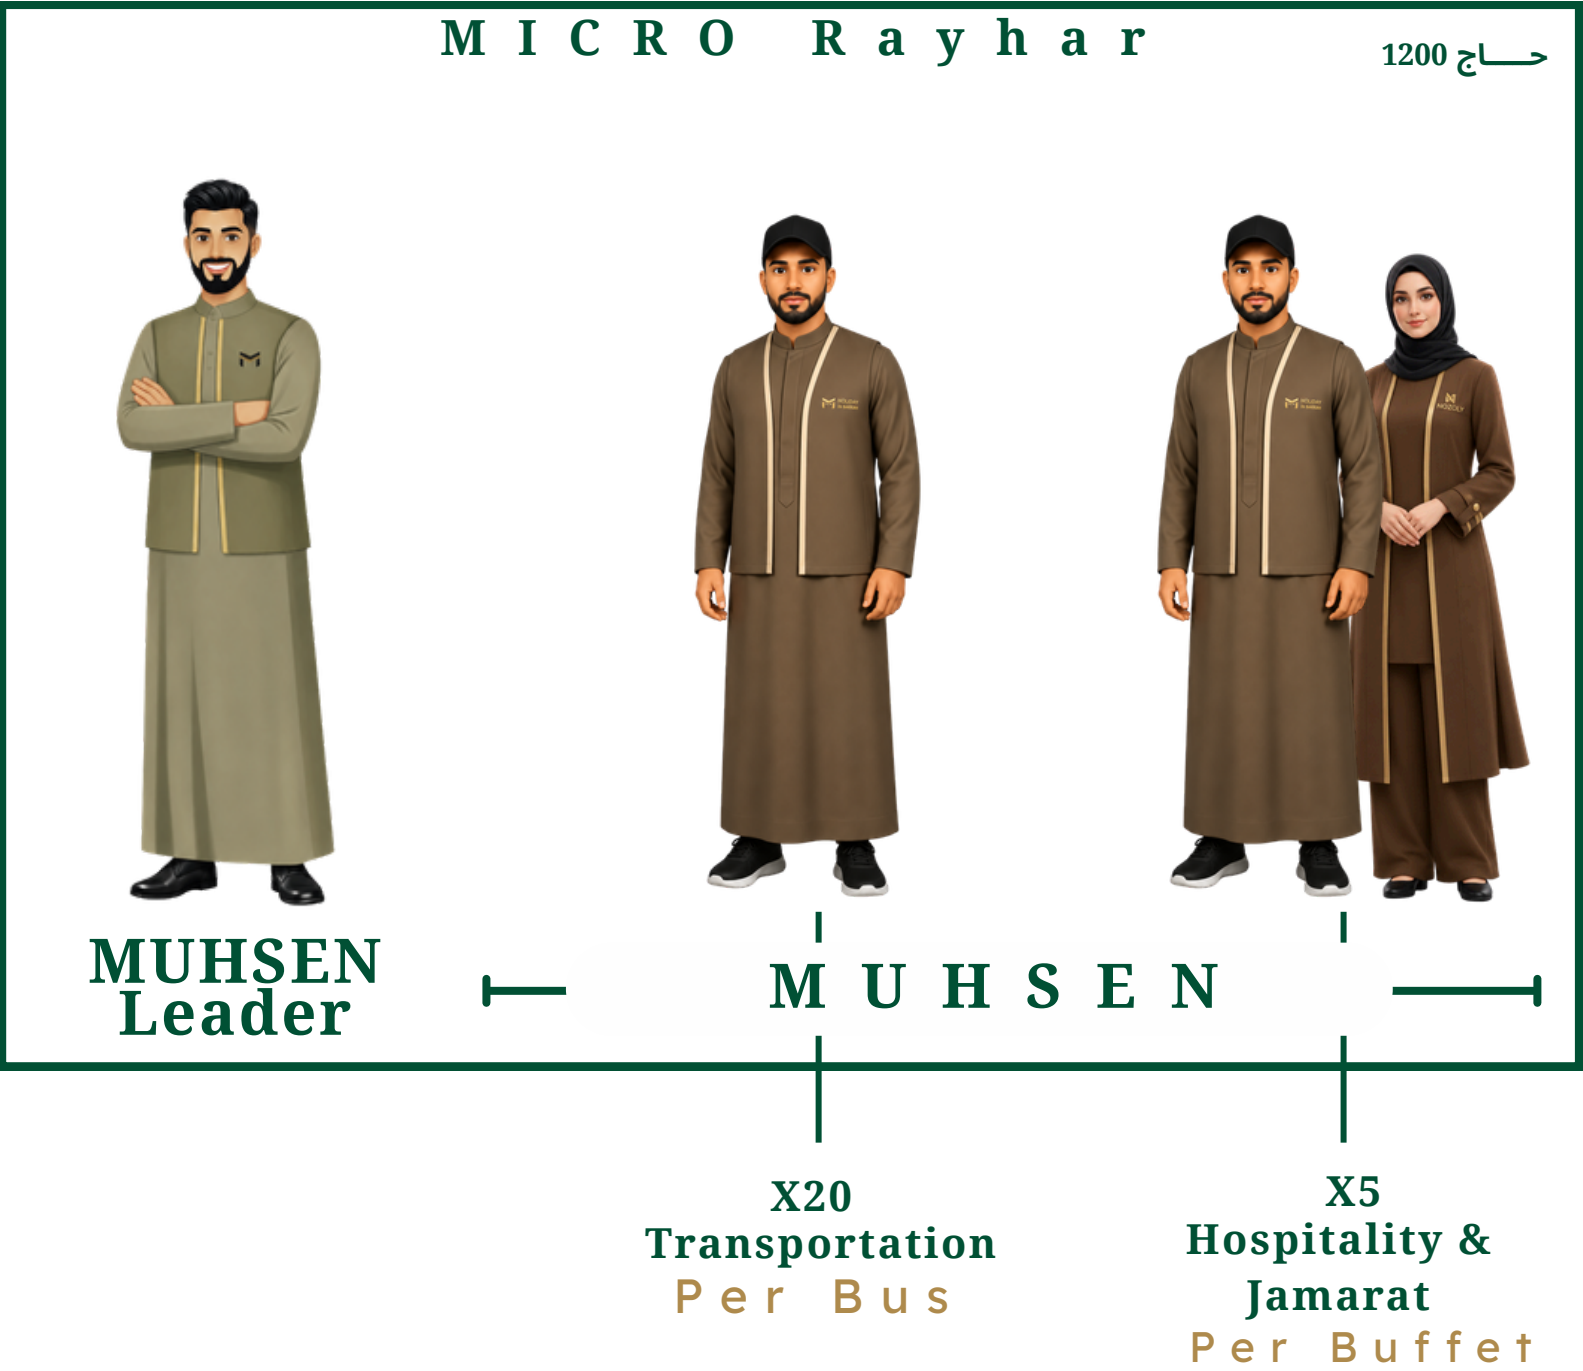

SECTION 04 - C.05 · MUHSEN OPERATION

Muhsen Teams in Numbers



MUHSEN
SPV

7



MUHSEN
Leader

140



MUHSEN
Bus

248



MUHSEN
Jamarat

140



MUHSEN
Hospitality

280

Total 815

SECTION 04 - C.05 · MUHSEN OPERATION

Six phases coordinate the workforce from Arafat deployment through final return to Makkah

Operational timeline showing workforce distribution across all deployment phases



Deployment Phases

- 1

Deployment to Arafat
Initial Deployment to Arafat
- 2

Departure to Muzdalifah
Movement from Arafat
- 3

Muzdalifah to Mina
Transition to Mina
- 4

Day 11
Jamarat Operations
- 5

Day 12
First Nafr
- 6

Day 13
Second Nafr

Reported Location Snapshot

Phase	Arafat	Mina	Muzdalifah	Makkah	Total
Phase 1	390	88	0	0	478
Phase 2	171	164	76	0	478
Phase 3	81	164	76	0	478
Phase 4	81	240	0	0	478
Phase 5	0	158	0	163	321
Phase 6	0	0	0	242	242



Personel in transit may not appear in every location subtotal.

SECTION 04 - C.05 · MUHSEN OPERATION

Phase 1 concentrates 390 Muhsen personnel in Arafat

Initial deployment to Arafat with Mina staging



Hotel / Makkah → Arafat
Movement via Mina staging area

Arafat : 380

Mina: 88

Total: 478

Deployment Assignment



Muhsen Supervisor
LEADERSHIP

From the hotel, move to the mashhaer with the last bus

5



Muhsen Leader
SUPPORT

Move to the mashaer with the first bus

76



Muhsen Transport
TRANSPORT

Operate shuttle movements until the phase is complete

157



Muhsen Jamarat
OPERATION

Deploy to Mina on 6 Dhu al-Hijjah

88



Muhsen Hospitality 1
HOSPITALITY

Remain at the hotel; headcount decreases progressively

76



Muhsen Hospitality 2
HOSPITALITY

Deploy to Arafat on Day 6

76

SECTION 04 - C.05 · MUHSEN OPERATION

Phase 2 splits the workforce across Arafat, Muzdalifah, and Mina

Departure from Arafat to Muzdalifah with Mina support



Arafat → Muzdalifah
Movement via Mina staging area

Arafat : 171

Muzdalifah: 76

Mina: 164

Total: 478

Deployment Assignment



Muhsen Supervisor
LEADERSHIP
Remain in Arafat

5



Muhsen Leader
SUPPORT
Move to Muzdalifah

76



Muhsen Transport 1
TRANSPORT
Operate shuttle movements until the phase is complete

67




Muhsen Transport 2
TRANSPORT
Remain in Arafat

90



Muhsen Jamarat
OPERATION
Remain in Mina

88



Muhsen Hospitality 1
HOSPITALITY
Move to Mina in the afternoon of Day 9

76



Muhsen Hospitality 2
HOSPITALITY
Remain in Arafat

76

SECTION 04 - C.05 · MUHSEN OPERATION

Reception teams stage in Mina while transport closes the movement phase

Muzdalifah → Mina; selected transport returns to Makkah



Muzdalifah → Mina
Selected transport returns to Makkah

Arafat : 81

Muzdalifah: 76

Mina: 164

Total: 478

Deployment Assignment

Muhsen Supervisor
LEADERSHIP
From the hotel, move to the mashhaer with the last bus

5

Muhsen Transport 1
TRANSPORT
Operate shuttle movements until the phase is complete

67

Muhsen Jamarat
OPERATION
Prepare to receive pilgrims in Mina

88

Muhsen Hospitality 2
HOSPITALITY
Remain in Arafat

76

Muhsen Leader
SUPPORT
Transition progressively to Mina

76

Muhsen Transport 2
TRANSPORT
Return to Makkah

90

Muhsen Hospitality 1
HOSPITALITY
Prepare to receive pilgrims in Mina

76

SECTION 04 - C.05 · MUHSEN OPERATION

Day 10-11 prioritizes Jamarat operations and Mina hospitality

Mina operations active; transport teams return to Makkah



Mina Operation Active
Selected transport returns to Makkah

Arafat : 81

Mina: 240

Total: 478

Deployment Assignment

Muhsen Supervisor
LEADERSHIP
Remain in Arafat

5

Muhsen Transport 1
TRANSPORT
Return to Makkah

67

Muhsen Jamarat
OPERATION
Support the stoning of the Jamarat

88

Muhsen Hospitality 2
HOSPITALITY
Provide hospitality support in Mina

76

Muhsen Leader
SUPPORT
Supervising Operation in Mina

76

Muhsen Transport 2
TRANSPORT
Return to Makkah

90

Muhsen Hospitality 1
HOSPITALITY
Move to Arafat

76

Mina Operation
OPERATION
Total Personel Stay in Mina

240

SECTION 04 - C.05 · MUHSEN OPERATION

Day 12 initiates First Nafr and shifts teams toward Makkah ,We have a total of 79 Mohsen Transport ready for the second Nafr in Makkah

First Nafr in progress - Mina to Makkah transition



Mina → Makkah
First Nafr in progress

Mina: 236

Makkah: 242

Total: 478

Deployment Assignment

Muhsen Supervisor
LEADERSHIP
Return to Hotel

5

Muhsen Leader 2
SUPPORT
Transition progressively to Makkah

38

Muhsen Jamarat 1
OPERATION
Decrease progressively according to KT

44

Muhsen Hospitality 1
HOSPITALITY
Decrease progressively according to KT

76

Muhsen Leader 1
SUPPORT
Supervising Operation in Mina

38

Muhsen Transport 1
TRANSPORT
Support the first Nafr

78

Muhsen Jamarat 2
OPERATION
Remain in Mina

44

Muhsen Hospitality 2
HOSPITALITY
Remain in Mina

76

SECTION 04 - C.05 · MUHSEN OPERATION

Phase 6 completes Second Nafr and consolidates 242 personnel in Makkah

Final phase: Mina/field deployment → Makkah and hotel



Mina → Makkah and Hotel
Second Nafr completion and consolidation

Makkah: 242

Total: 242

Deployment Assignment

Muhsen Supervisor
LEADERSHIP
Hotel

5

Muhsen Leader
SUPPORT
Transition progressively to Makkah

38

Muhsen Transport
TRANSPORT
Support the Second Nafr

79

Muhsen Jamarat
OPERATION
Decrease progressively according to KT

44

Muhsen Hospitality
HOSPITALITY
Decrease progressively according to KT

76



Complete the return, confirm hotel accountability, and close field deployment

SECTION 04 - D · CONTROL & COMMAND CENTER

24-Hour Monitoring and Analysis

01

Real-Time Monitoring

Serving as the nerve center for real-time monitoring of all Hajj activities, including crowd movements, transportation, healthcare services, and security operations, to facilitate swift decision-making and coordination.

02

Crisis and Emergency Management

Acting as the main hub for managing emergencies and unexpected incidents by coordinating response efforts among relevant agencies, deploying resources rapidly, and ensuring the safety of pilgrims.

03

Pilgrim Movement Management

Maintaining continuous communication channels with various operational units, service providers, security personnel, and government agencies to ensure seamless information flow and situational awareness.

Decision Support for Departments

Monitoring adherence to schedules and operational guidelines, ensuring that all activities are aligned with safety standards and logistical plans.

04

Post-Hajj Analysis and Reporting

Generating detailed incident reports, operational summaries, and performance analytics to inform decision-making and future planning.

05

SECTION 04 - E.01 · NUSUK CARD

Hajj Nusuk Card Distribution Process

Distributing the Nusuk Card to Pilgrims' Countries

Ensure that the distribution process of nusuk cards for pilgrims in the country is organized and operates efficiently and effectively.

01 Printing NUSUK Cards

- Verify pilgrim data accuracy.
- Grouping pilgrims (max 200 per batch).
- Track ticket issues.
- Order NUSUK Card printing.
- Submit progress reports to Hajj Mission & HAJJ INN management.

02 Receiving NUSUK Cards

- Track delivery and ensure completeness.
- Organize cards as per order.
- Submit progress reports to Hajj Mission & HAJJ INN management.

03 Distributing NUSUK Card

- Coordinate with logistics partners for secure delivery.
- Ensure safe storage upon arrival in pilgrims Country.
- Submit progress reports to Hajj Mission & HAJJ INN management.

04 Activation NUSUK Cards

- Prepare distribution area and staff.
- Hand over cards to pilgrims with photo evidence.
- Activate distributed cards.
- Submit progress reports to Hajj Mission & HAJJ INN management.

SECTION 04 - E.02 · NUSUK CARD

Employee Nusuk Card Distribution Process

Nusuk Card for Employee

Ensure that the distribution process of nusuk cards for pilgrims in the country is organized and operates efficiently and effectively.

01 Ajeer Submission

Employee Data Verification and Ajeer Process

- Verify employee data
 - Iqamah
 - Makkah Entry Permit
 - Ensure there are no Ajeer agreements with other companies
- Ajeer submission process
- Ajeer approval

02 Nusuk Submission

- Confirm employee administration details
- Provide information via Nusuk Masar
- Track the approval process from the Ministry

03 Nusuk Printing


- Ensure the accuracy of pilgrim data.
- Organize employees into groups (maximum of 200 per batch).
- Monitor ticket-related issues.
- Arrange for the printing of NUSUK Cards.

04 Nusuk Activation

- Confirm the accuracy of staff data.
- Distribute cards to staff along with photo verification.
- Activate the issued cards.
- Provide progress reports to the department and companies.

We succeed only when
every department **operates**
as one.


An integrated system connects every department,
aligns every process, and truns shared
information into coordinated action.

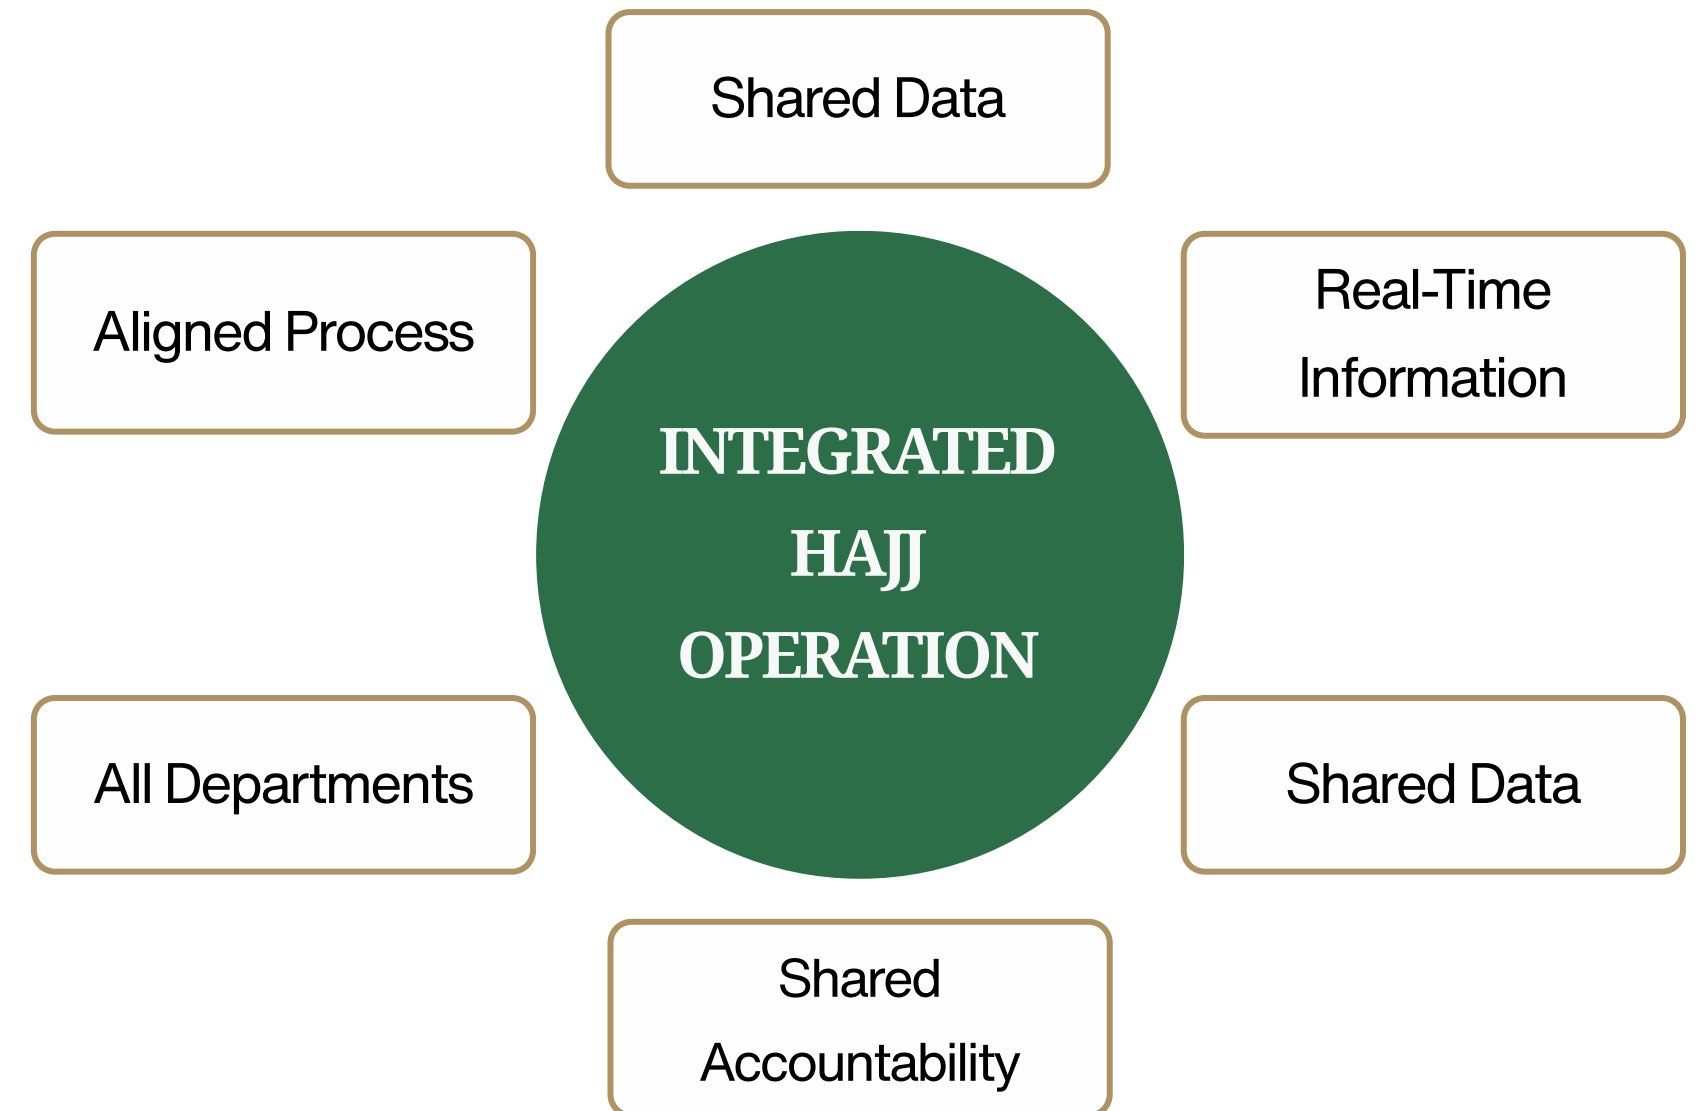

ONE SYSTEM. **ONE TEAM.** ONE MISSION.



MUHSEN
Leader

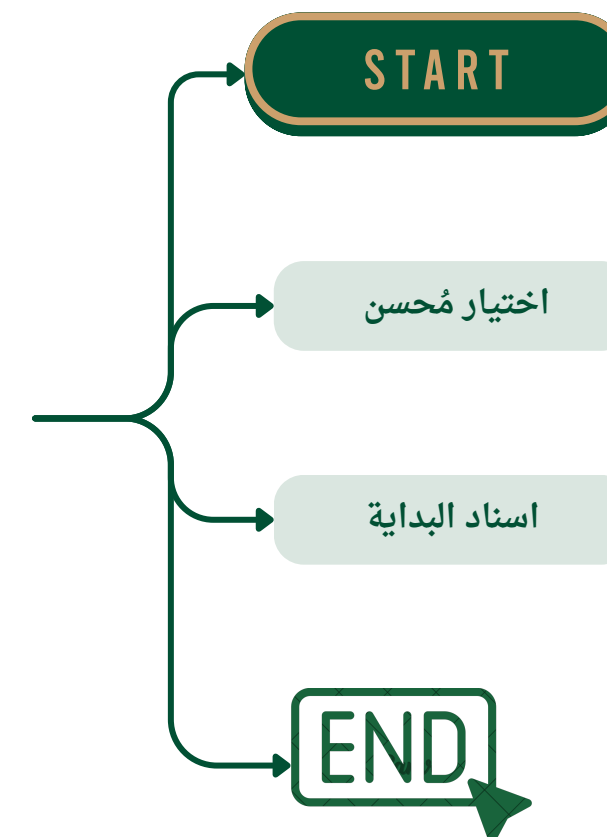

1. تفاصيل المهمة - اختيار المحسنين

يختار الليدر المحسنين التي يحضرون معه

9:41

تفاصيل المهمة



خدمة ضيوف الرحمن
توجيه الحاج - باب الملك فهد
المسجد الحرام - الدور الأرضي

جارية

رقم المهمة	تاريخ المهمة	وقت المهمة	مدة المهمة
#1258	1445/12/20	08:00 ص إلى 02:00 م	6 ساعات

بدء المهمة

يمكن بدء المهمة بعد حضور المحسنين

اختر المحسنين التي يحضرون معك (2/2)

يجب اختيار 2 محسن من أصل 5

☒

أحمد عبدالله
#1001

☒

محمد السبيعي
#1002

☐

خالد الزهراني
#1003

☐

عبدالله العتيبي
#1004

☐

فهد المطيري
#1005

المهمة سيظهر فقط للمحسنين المختارين

(إن إسناد البداية اختياري)
يمكنك إسناد بدء المهمة لأحد المحسنين المختارين

اختر محسن إسناد بداية المهمة

إنهاء المهمة

حفظ الاختيارات

الرئيسية

المهام

الإشعارات

التقارير


المزيد

2. تفاصيل المهمة - بعد الاختيار

عرض المحسنين المختارين وحالة الحضور وإمكانية إسناد البداية

9:41

تفاصيل المهمة



خدمة ضيوف الرحمن
توجيه الحاج - باب الملك فهد
المسجد الحرام - الدور الأرضي

جارية

رقم المهمة	تاريخ المهمة	وقت المهمة	مدة المهمة
#1258	1445/12/20	08:00 ص إلى 02:00 م	6 ساعات

بدء المهمة

يمكن بدء المهمة الآن

تحديث اختيار المحسنين

المحسنين المختارين (2)

☒

أحمد عبدالله
#1001

☒

محمد السبيعي
#1002

إن إسناد بداية المهمة

☒

أحمد عبدالله
#1001

تم إسناد بداية المهمة إلى أحمد عبدالله

يمكنك صلاحية بدء المهمة

إنهاء الإسناد

إنهاء المهمة


الرئيسية

المهام

الإشعارات

التقارير

المزيد

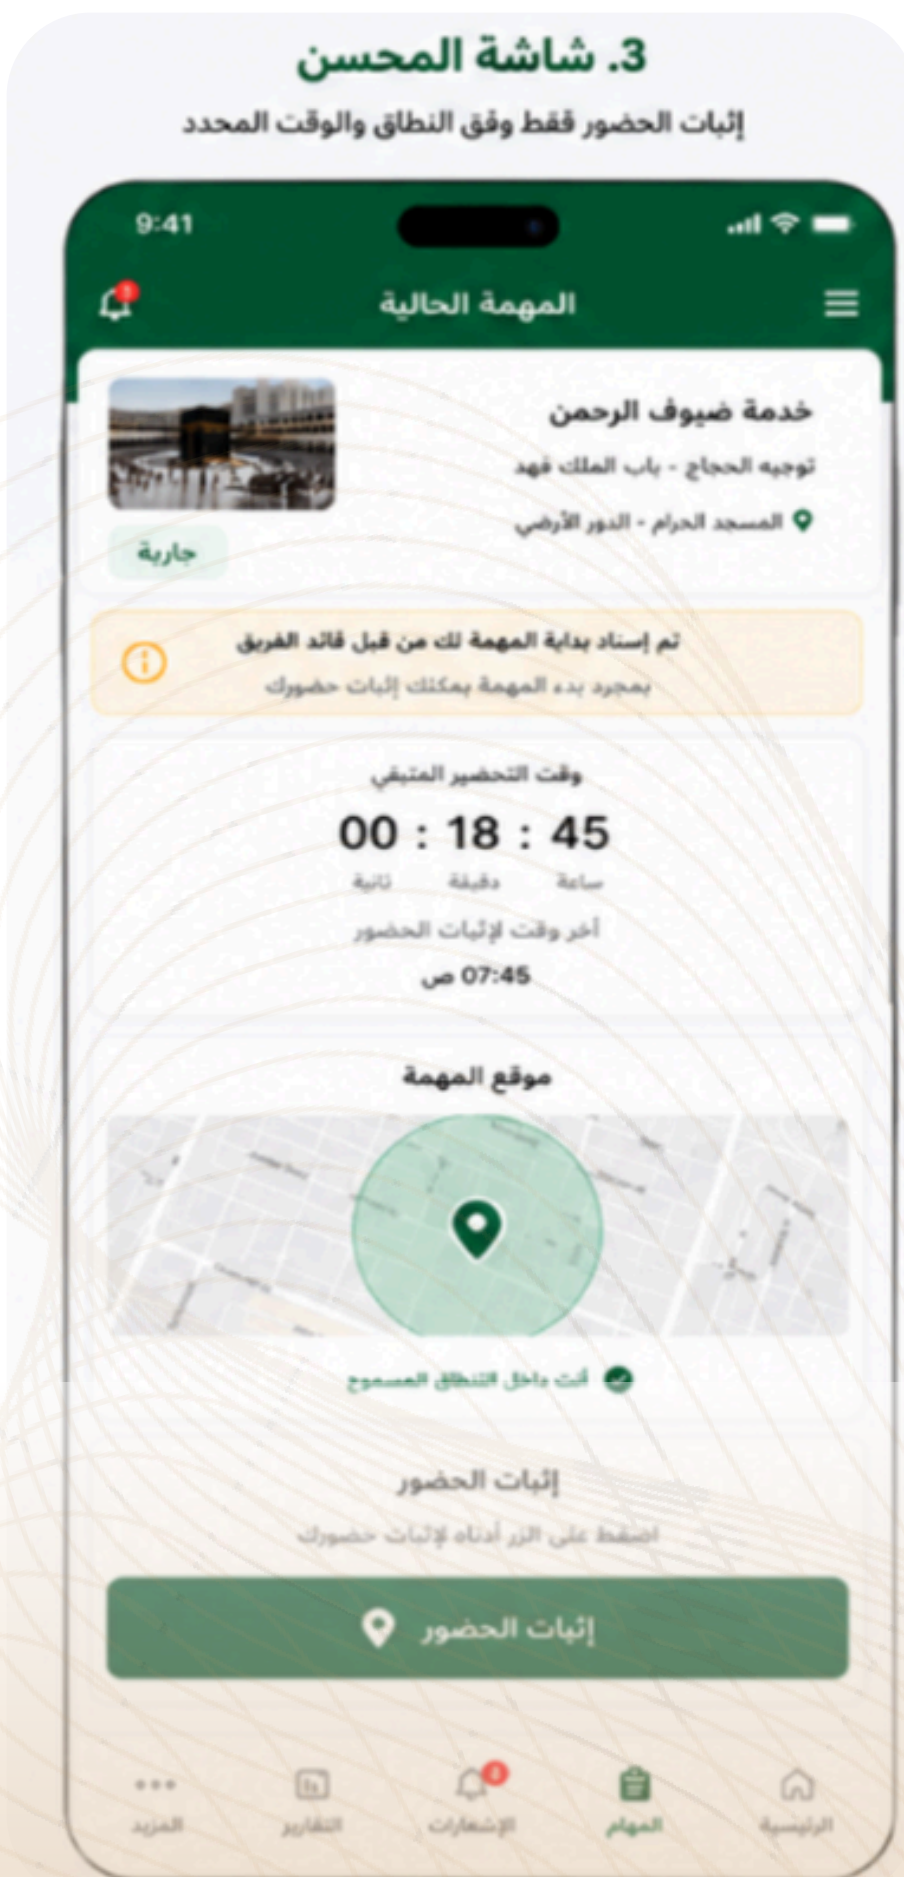

M U H S E N



Jamarat



Transportation



Hospitality

اثبات حضور

بدا المهمة في حال تم
اسناد البداية له

رفع بلاغات

استقبال تذاكر
